Downtown Flagler Street Beautification Project

Recap of work done in the month of April 2024

Construction Recap: April 2024

Phase A (Biscayne Blvd to E 3rd Avenue)- Substantial Completion

- Working on Punch List items:
- Cleaning manholes on roadway in various locations (Punchlist item).
- Cleaning drainage grate in various locations (Punchlist item).
- Sealing bases of street lighting in various locations (Punchlist item).
- Sealing street sign base in various locations (Punchlist item).
- Installed sidewalk pavers for curb ramp on the Southwest corner of Biscayne Blvd.
- Installed directional pavers and addressed punch list items for curb ramp on NW corner of Biscayne Blvd (Rework).
- Placed concrete for SW corner of Biscayne Blvd for detectable warning.
- Watering oak and palm trees.
- Removing section of asphalt on crosswalk on Biscayne Blvd.
- Placed FC 9.5 (SPM22-20255A) asphalt mix for crosswalk on Biscayne Blvd.

Construction Recap: April 2024

Phase B (E 3rd Avenue to E 2nd Avenue)- Substantial Completion

- Working on Punch List items:
- Sealing bases of street lighting in various locations (Punchlist item).
- Sealing street sign base in various locations (Punchlist item).
- Repairing sidewalk pavers in various locations (Punchlist item).
- Installing delineating sidewalk pavers on the SE corner of 2nd Ave (Punchlist item).
- Addressing punch list items and bolting tree grates.
- Watering oak and palm trees.
- Repairing irrigation line in various locations.

Phase C (E 2nd Avenue to 1st Avenue)

- Working on Punch List items:
- Relocation of irrigation bubblers and sprinkler head in planter and tree pit area in various locations (Punchlist item).
- Spreading polymer sand on the North and South side sidewalk pavers in various locations. (Punch list item).
- Repairing spalls on the trench drain in various locations (Punch list items).
- Repairing sidewalk pavers in various locations. (Punch list item).
- Testing irrigation systems (Punch list item).
- Painted mast arm on 2nd Ave section C (Punch list item).

- Phase C (E 2nd Avenue to 1st Avenue)
- Installing pipes for irrigation system in various locations.
- Installing roadway pavers for crosswalk (Rework).
- Watering oak and palm trees.
- Trimming fronds on palm trees.
- Installing pipe connections to test irrigation system on North side of Section C.
- Removing excess material in planter and tree pit area in various locations.

- Loading and hauling hardscape furniture to section D.
- Boring holes for hardscape furniture.
- Installing anchor bolts on to hardscape furniture.
- Installing tree grates in various locations.
- Installing sidewalk pavers in deterrent area.
- Placed black concrete for sidewalk bands. Installing plants in planters in various locations.
- Installing tree grates in various locations.
- Installed pull boxes on the NW corner of 1st Ave.
- Cleaning drainage structures throughout section D.
- Demolished sidewalk on the NE corner.
- Adjusted pull boxes on the NE corner.
- Installed sidewalk rail on the NE corner.
- Placed concrete for sidewalk on the NE & NW corner of section D.




Phase A (Biscayne Blvd to E 3rd Ave) Asphalt repair on crosswalk at Biscayne Blvd

Phase B (E 3rd Ave to 2nd Ave)

• Repairing tree grates



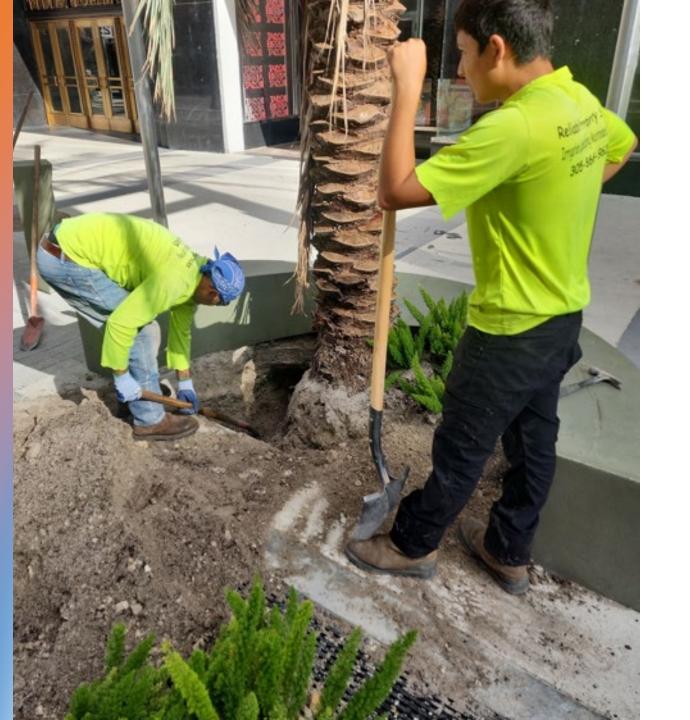

Phase C (E 2nd Ave to 1st Ave)

• Repairing irrigation lines

Phase C (E 2nd Ave to 1st Ave)

· Installation of landscaping





• Finishing concrete work

• Installation of sidewalk pavers in deterrent area.

• Boring holes for installation of Hardscape furniture





• Installing forms for concrete sidewalk

 Installation of hardscape furniture





• Leveling manhole to finish grade



• Grading sidewalk material

• Grading and compacting sidewalk material

